


CALIFORNIA PUBLIC UTILITIES COMMISSION

California Advanced Services Fund Rural and Urban Regional Broadband Consortia Grant Program



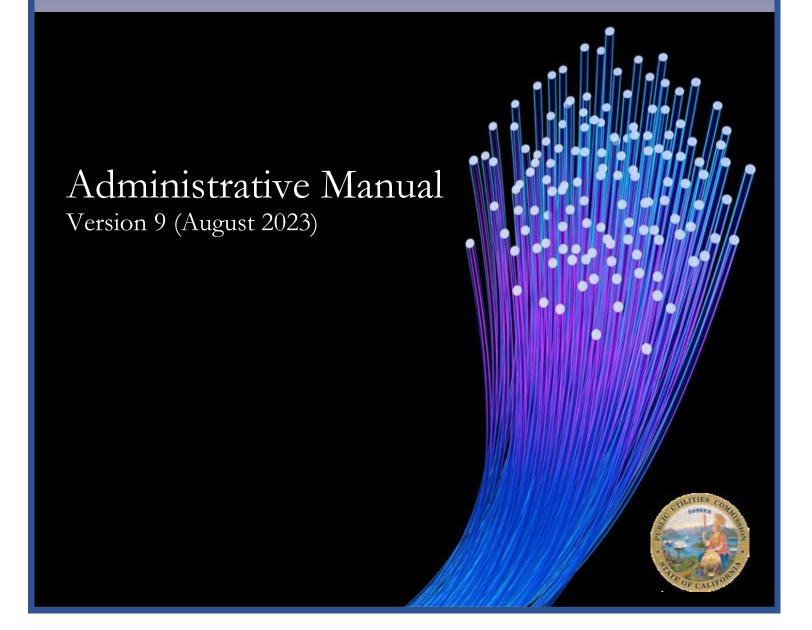

To all CASF Regional Consortia:

The California Public Utilities Commission (CPUC or the Commission) thank you for your interest in promoting broadband deployment in California. We welcome you to the California Advanced Services Fund (CASF) Program and look forward to working with you to help bridge the digital divide in California.¹

Respectfully,

The CASF Team
CPUC Communications Division

¹ This Administrative Manual was prepared by California Public Utilities Commission (CPUC) CD staff. It does not change, replace, or waive any of the rules or guidelines adopted in Decision (D.) 22-05-029 on May 19, 2022, nor has the CPUC passed upon the accuracy or adequacy of the information in it. The contents of the manual are for informational proposed only.

TABLE OF CONTENTS

I.	Introduction	1
II.	CASF Staff Team	1
III.	Application Checklist and Requirements	1
IV.	Grant Disbursement Schedule Form, Consent Form, and Payee Data Record	2
V.	Performance	3
VI.	Changes to a Consortium's Work Plan	3
VII.	Bi-annual Progress Reporting	4
A.	Submission of Bi-annual Progress Report	4
B.	Bi-annual Progress Reporting Timeline	6
VIII.	Progress Payment Requests	6
A.	Disbursement of Grant Funding	6
B.	Progress Payment Requests	6
C.	Final Payment and Project Completion Reports	8
IX.	Reimbursement for Public Workshop	9
X.	Annual Audit	9
XI.	Regular Meetings	9
XII.	Payment Processing	9
XIII.	Publicity and Acknowledgment	. 11
Appen	dix A: Application Package	. 12
Appen	dix B: Consortia Grant Forms	. 26
Appen	dix C: Bi-annual Progress Report and Payment Request Package	. 32
Appen	dix D: Annual Audit Report Template for Reporting Activity Information	. 11

I. Introduction

The purpose of this Administrative Manual (Manual) is intended solely for providing guidance for applicants applying for the CASF Rural and Urban Regional Broadband Consortia Grant Account (Consortia Grant Account) funding and for the CPUC Communications Division (CD) staff's oversight of the consortia's operations applicable to Consortia Grants.

Pertinent documents include the following CPUC decisions and resolutions which are also hyperlinked on the CPUC Consortia webpage:

- Decision (D.) 22-05-029 establishes current rules, requirements, and guidelines for the Consortia Grant Account.
- D.18-10-032 implemented programmatic changes to the Consortia Grant Account as required by Assembly Bill (AB) 1665 and established the requirements and guidelines for the 2019, 2020, and 2021 Consortia Grant Cycles.
- <u>D.11-06-038</u> established the requirements and guidelines for the 2016 Consortia Grant Cycle.

For more information, please visit the <u>Consortia Grant Account program website</u>, or send an email to CASF_Consortia_Grant_Administrator@cpuc.ca.gov.

II. CASF Staff Team

The CD CASF Consortia Grant Account Team is responsible for overseeing the CASF Consortia Grant Account program. Questions may be directed to the following:

 Rural and Urban Regional Broadband Consortia Account <u>CASF Consortia Grant Administrator@cpuc.ca.gov</u>

III. Application Checklist and Requirements

Appendix A, *Application Package*, to this Manual provides CASF Consortia Grant application form templates illustrating key informational requirements and documents that must be properly completed and submitted with the application to be considered for approval. The *Application Package* forms are as follows and are available in Excel format:

- **Appendix A-1** CASF Consortia Grant Application Checklist
- **Appendix A-2** Description of Existing and Past Non-CASF Funded Projects
- **Appendix A-3** Board Member Background and Project Role
- **Appendix A-4** Work Plan and Performance Metrics Plan
- **Appendix A-5** Proposed Detailed Budget

• **Appendix A-6** – *Affidavit Form*.

The CASF Consortia Grant Application Checklist lists the required information items, with references to the D.22-05-029 Sections. Each Consortium applicant must submit all appendixes above as part of the application, along with supporting information.²

The Work Plan and Performance Metrics Plan should identify the Consortium's goals as they relate to the region's needs for broadband deployment and include detailed functions and activities related to implementation of each goal. The Work Plan is to be tailored to fit the needs of a given region's constituents and geography, incorporating core responsibilities, including goals, measurable deliverables, expected outcomes, and specific timeline milestones as they relate to broadband deployment. The Work Plan and Performance Metrics Plan should also explain how the performance results from the proposed functions and activities will be tracked and measured, following milestone dates as described in the Work Plan. Appendix A-4, Work Plan and Performance Metrics Plan, illustrates the form template format, and provides examples of activities, deliverables, performance measures, and work plan terminology definition and requirements.

IV. Grant Disbursement Schedule Form, Consent Form, and Payee Data Record

The Consortia grantee will be contacted following approval of a CASF Consortia grant award. CD staff will request each grantee to complete and submit a *Grant Disbursement Schedule Form*, a *Consent Form*, and a *Payee Data Record (STD 204)* if not already on file with the Commission. A copy of the *Grant Disbursement Schedule Form* and *Consent Form*, as well as a hyperlink to STD 204 is attached as **Appendix B**, *Consortia Grant Forms*.

The *Grant Disbursement Schedule Form* lists due dates based on approval date of the grant award for bi-annual progress reports and bi-annual payment requests of the grant for the Consortium. A completed STD 204 is required when receiving payment from the State of California and information provided in this form will be used by the Commission to prepare Information Returns, i.e., Internal Revenue Service, Form 1099.

Grantees are required to sign a *Consent Form* which binds the grantee to the terms, conditions, and requirements of the Decision and the Resolution, as well as all CASF rules, including those in the Consortia Grant Account Requirements, Guidelines and Application Materials awarding the grant. Should the grantee not accept the award through failure to submit the consent form within 30 calendar days from the date of the award, the Commission will deem the grant null and void. The proposed wording of the consent form is available on the CASF Consortia website,

-

² D.22-05-029, Appendix 3, p. 5.

The Commission will not initiate payment for the Consortium's activities until CD staff receives the *Grant Disbursement Schedule Form*, *Consent Form*, and *Payee Data Record* (if applicable). In order to receive a progress payment, the grantee must first submit the Progress Report to CD staff, together with the request for payment and reimbursement supported by relevant documentation such as invoices and a signed affidavit that activities have been completed consistent with approved plans, etc.

V. Performance

By receiving a CASF Consortia grant, the grantee agrees to comply with the terms, conditions, and requirements of the grant and submits to the jurisdiction of the Commission with regard to disbursement and administration of the grant.³ All performance specified under the terms of any award shall be completed on or before the termination date of the award as stated in the Resolution authorizing the award. The start of the Consortia grant begins upon grant approval.⁴ Should the grantee or its contractor fail to commence work at the agreed upon time, the Commission may terminate the award and may impose penalties.⁵ In the event that the grantee fails to complete the project, in accordance with the terms of approval granted by the Commission, the grantee will be required to reimburse some or all of the CASF funding that it has received.⁶ If the Consortia grantee fails to perform in good faith, or in accordance with the expectations set forth in its *Work Plan and Performance Metrics Plan*, as affirmed in its *Affidavit Form*, the Commission may withhold subsequent grant disbursement, suspend, or terminate the Consortia grant, as warranted.⁷

Each Consortia grantee must use the grant funding solely for the approved project as described in the Grantee's Commission approved *Work Plan and Performance Metrics Plan* as affirmed by the signed *Affidavit Form*. Each Consortia grantee must complete the project in accordance with and within the project performance period set forth in the Commission approved *Work Plan*⁸, see Section IV, Changes to a Consortium's *Work Plan*, below, on changes to the substantive terms and conditions underlying Commission approval. Grantee's performance and completion of the project must comply with all applicable laws and regulations. Grantees must notify the CD as soon as they become aware that they may not be able to meet performance metrics set forth in the *Work Plan and Performance Metrics Plan*.

VI. Changes to a Consortium's Work Plan

³ D.22-05-029, Appendix 3, p. 14.

⁴ Id. at p. 12.

⁵ Id. at p. 14.

⁶ Id.

⁷ Id.

⁸ D.22-05-029, Appendix 3, p. 12.

Proposed Change

Consortia Action

Any changes to the substantive terms and conditions underlying Commission approval of the grant (e.g., changes to the Work Plan, budget, or designated Fiscal Agent, etc.) must be communicated in writing to the Director of Communications Division at least 30 days before the anticipated change and may be subject to approval by either the Director or by Commission resolution before becoming effective. The table, on the next page, shows typical changes and the actions to be taken to initiate review for approval.

VII. Bi-annual Progress Reporting

Consortia are required to submit bi-annual progress reports. The *Bi-annual Progress Reports* shall be based upon the approved Work Plan and Performance Metrics Plan, Consent Form, timelines, milestones, and costs identified in the application. Further, the Bi-annual Progress Reports should indicate the actual date of completion for each task/milestone as well as problems/issues encountered, and the actions taken to resolve these problems/issues. A sample Bi-annual Progress Report template and Start-up Period Report is included as **Appendix C-3**. The Bi-annual Progress Reports must be submitted and certified under penalty of perjury by using the Bi-annual Report and Payment Request Transmittal Letter and Declaration (see Appendix C-1). All grantees must submit bi-annual progress reports on the status of the project irrespective of whether progress payment is requested.

In order to receive progress payment, each consortium must submit a Bi-annual Progress Report to CD staff together with a *Bi-annual Progress Payment Request* supported by relevant documentation and a signed affidavit¹¹ as explained in Section VIII, Bi-annual Progress Payment Requests, below.

Submission of Bi-annual Progress Report A.

The Bi-annual Progress Report and any Progress Payment Request must be submitted electronically.

For electronic submissions, please send to: CASF_Consortia_Grant_Administrator@cpuc.ca.gov

The Commission's firewall may prevent consortia from successfully sending large electronic data files over standard email services to the Consortia Grant Administrator. Using the secure

⁹ D.22-05-029, Appendix 3, p. 14.

¹⁰ Id. at p. 11.

¹¹ Id. at p. 11; see also D.22-05-029, Appendix 3, p. 12.

Work Plan and Performance Metrics Plan (WP) - Tasks - Activities - Deliverables - Performance measures - Timeline	All changes to WP are considered substantive, per D.22-05-029. Need Commission and/or Director approval prior to becoming effective. Submit document(s), including proposed revised Budget, if affected, at least 30 days before the anticipated change to the Consortia Grant Administrator with a cover letter addressed to the CD Director explaining requesting approval of the change.
Budget Allocation	All changes to Budget are considered substantive, per D.22-05-029. Need Commission and/or Director approval prior to becoming effective. Submit documents at least 30 days before the anticipated change to the Consortia Grant Administrator with a cover letter addressed to the CD Director explaining requesting approval of the change.
Designated Fiscal Agent - Agency entity/organization - Representative	All changes to Fiscal Agent are considered substantive, per D.22-05-029. Need Commission and/or Director approval prior to becoming effective. Submit to the Consortia Grant Administrator with a letter addressed to the CD Director at least 30 days before the anticipated change explaining the change and new fiscal agent recommendation and requesting approval of the change: - Must submit a new Letter Committing to Act as Fiscal Agent (see Appendix A-1, CASF Consortia Grant Application Checklist, Item 15, for the letter requirements) and a new Affidavit Form (see Appendix A-6), when a new fiscal agent entity is proposed. - Must include a description of the proposed fiscal agent entity/organization or a bio describing new representative's relevant experience.
Official Membership - Add/remove agency(ies) and/or representative(s) - Other changes	Revise membership list; and notify the Consortia Grant Administrator in email explaining changes, including an updated membership list.
Key Contact for Consortium - Representative(s) - Other changes	Notify the Consortia Grant Administrator in email explaining changes and new representative(s), including a bio or professional/education experience description of the new representative(s).

FTP Server will allow you to send files up to 2 GB in size. Go to: https://cpucftp.cpuc.ca.gov/ to initiate new user registration using your email address and follow the steps to complete your account set up. Thereafter, you can go to the hyperlink site, log in, attach files, and send them to the Consortia Grant Administrator.

B. Bi-annual Progress Reporting Timeline

The start date of the consortium grant will begin upon grant approval. The *Bi-annual Progress Report* is required every six months, i.e., at the end of the six-month period, at the end of the 12-month period, at the end of the 18-month period, of deployment, at the end of the 24-month period, etc. Each Consortium must submit their *Bi-annual Program Reports* by no later than three months after every six months.

VIII. Progress Payment Requests

The Consortia Grant program's disbursement of grant funding process contained herein is in accordance with the guidance set forth in D.22-05-029, Resolutions approving Consortia grants, and the State Administrative Manual (SAM).

A. Disbursement of Grant Funding

All progress payment requests must be submitted together with the *Bi-annual Progress Report* and must be supported by documentation such as receipts and/or invoices for services rendered and a signed affidavit that activities have been completed consistent with approved plans. The disbursement of funding at any time is subject to Commission discretion, including a review and approval process of each grantee through regular site visits, progress reports and supporting invoice and receipts. Disbursements of grant funding will be made to the Fiscal Agent.

A grantee may request reimbursement of start-up costs up to 25% of entire approved grant prior to its first Bi-annual Progress Payment Request. If a grantee requests an initial start-up cost payment, then a "Start-up Period Report" is required. Such request must be supported by documentation, e.g., receipts, invoices, quotes, etc. The Start-up Period Report must be submitted no later than three months after the completion of the start-up activities. Subsequent disbursements are on a bi-annual progress report-review basis.

B. Progress Payment Requests

6

¹² D.22-05-029, Appendix 3, p. 11.

In order to receive a progress payment, the Consortium must submit the required forms, as illustrated in **Appendix C**, *Bi-annual Progress Report and Payment Request Package*, to the CD supported by documentation, e.g., invoices, quotes, receipts, a signed affidavit, and an annual audit (i.e., for annual year-end payment request).

Each payment request package must consist of the following documents (available in Excel format):

- Appendix C-1 Bi-annual Report and Payment Request Transmittal Letter and Affidavit

 Appendix C-2 Bi-annual Payment Request Cover Sheet: summarizing expenses claimed, and payments received thus far
- **Appendix** C-3 *Bi-annual Progress Report*: is the main document for reporting actual progress made during the reporting period, including activities performed, deliverables completed, timeline milestone achieved, and actual performance measures met
- Appendix C-4 Bi-annual Payment Request Worksheet: is the main document for input and listing of expenses.
 - Allowable Expenses: shall be for consortia activities directly related to and in support of CASF-funded infrastructure applications or broadband deployment projects related to the new programs created under SB 156 and AB 164 as set forth in D.22-05-029, Appendix 3, pp. . The CASF Consortia Grant Account funding is limited to Consortia activities directly related to and in support of CASF-funded infrastructure applications (i.e., an infrastructure application 100% funded by CASF funding, an infrastructure application funded by both CASF and non-CASF funding), or broadband deployment projects related to the new programs created under SB 156 and AB 164.
 - o <u>Travel Expense Claim and Business Expense Reimbursements</u>: each claimant must complete a form *STD-262A*, *Travel Expense Claim (TEC) Form*, and follow instructions therein. Expense claims must comply with the travel expense, limitation rules applicable to State of California employees and contractors. The allowable rates/costs are those negotiated and approved under the collective bargaining agreement(s) that are in use by State employees. An electronic copy of STD 262A, instructions as well as all current applicable information are available at: http://www.calhr.ca.gov/employees/pages/travel-reimbursements.aspx.
 - Non-Allowable Expenses: include, but are not limited to: (1) a Consortia Account grant shall not be used for meals, food and refreshments for group gathering(s) such as meetings, conferences, workshops, etc.; (2) a Consortia Account grant shall not be used for work on

_

¹³ http://hrmanual.calhr.ca.gov/Home/ManualItem/1/2201.

legislation, including meetings, travel, or lobbying; (3) a Consortia Grant shall not be used for construction of infrastructure facilities; (4) a Consortia Account shall not be used for adoption activities; and (4) a Consortia Account grant shall not be used to fund activities that are already funded by any other public or private sources.

The Annual Year-End Payment Request must include an annual audit of consortia program expenditures, prepared by an independent, licensed Certified Public Accountant (CPA) expressing a conclusion about the reliability of the primary financial/business functions of the Consortium.

C. Final Payment and Project Completion Reports

All performance specified under the terms of any award shall be completed on or before the termination date of the award. A project completion report is required showing that all activities in the approved Work Plan have been accomplished. The final payment will be equal to the outstanding balance due under the consortium grant or actual expenditures, whichever is less. The grantee's project completion report and final payment report should be submitted to the CD no later than three months after the project completion, and should include the following documents:

- Final Progress and Payment Request Transmittal Letter and Affidavit;
- Payment Request Cover Sheet;
- Final Progress Report;
- Final Payment Request Worksheet including all documentation and receipts;
- Annual Audit; and
- Project Completion Report.

D. Grant Oversight

Staff has the authority to initiate any necessary audit, verification, and discovery of Consortium members relating to grant funding activities to ensure that CASF Consortia grants are spent in accordance with the adopted rules and standards for the Consortia Grant Account. Each Consortia grantee shall maintain books, records, documents and other evidence sufficient to substantiate expenditures covered by the grant, according to generally accepted accounting practices. Each Consortia grantee shall make these records available to the Commission upon request and agrees that these records are subject to a financial audit by the Commission at any time upon request within five years after the Grantee incurred the expense being audited. A Consortia grantee shall provide access to the Commission upon 24-hour notice to evaluate work completed or being performed pursuant to the grant.

IX. Reimbursement for Public Workshop

All consortia receiving CASF grants shall attend at least one of the annual public workshops to be conducted by the CD. Consortia may claim reimbursement for travel expenses and per diem costs associated with each annual public workshop hosted by the CD. The maximum reimbursement allowable is \$2,000 per person for up to five delegates for each annual public workshop, for a total of up to \$10,000 per consortium. To request reimbursement, a *Public Workshop Reimbursement Request Form* attached as **Appendix C-5** must be completed and submitted along with the *Bi-annual Progress Payment Request*. For each delegate requesting reimbursement, a TEC Form STD 262A (see Section VIII, Bi-annual Progress Payment Request above) must be used.

X. Annual Audit

Each Consortium is required to conduct an annual audit of its expenditures for grant programs funded and submit to the Commission an annual report that includes both of the following:

- A description of activities completed during the prior year, how each activity promotes the deployment of broadband services, and the cost associated with each activity
- The number of project applications assisted.

To assist grantees to provide the required information, a template is included as **Appendix D**, *Annual Audit Report Template for Reporting Activity Information*.

The annual audit should be prepared by an independent, licensed certified public accountant (CPA) expressing a conclusion about the reliability of the primary financial/business functions of the Consortium. The annual audit should provide assurance that the consortium's financial statements are free of material misstatement and are fairly presented based upon the application of generally accepted accounting principles.

XI. Regular Meetings

The CD's Consortia Grant Administrator will schedule conference calls with all consortia on a regular basis. The Consortia Grant Administrator will establish the agenda and seek input from the Consortia. Representatives from each consortium are encouraged to participate in the conference calls.

XII. Payment Processing

The Consortia Grant Administrator will review payment requests comparing expenses against the Consortium's approved budgets, *Work Plan and Performance Metrics Plan*, timelines milestones, costs and activity/deliverable/performance measure accomplishments shown in the *Bi-annual Progress Report*

and *Bi-annual Payment Request*. The Consortia Grant Administrator may request additional information regarding the reports, expenses, and/or supporting documentation.

Upon approval, the CD will submit payment voucher documents to the Commission's Fiscal Office. The Fiscal Office will review all payment voucher submissions in accordance to the State Administrative Manual; and upon satisfactory review, will schedule payment with the State Controller's Office, which is responsible for issuing and distributing the check to the payee designated by the Commission, i.e. the Consortium's Fiscal Agent.

No payment will be made for any payment requests received three months after relevant reports are due (i.e., bi-annual progress reports, start-up period reports, and/or completion reports). 14

¹⁴ D.22-05-029, Appendix 3, p. 13.

XIII. Publicity and Acknowledgment

Any publications, studies, or reports made possible or derived in whole or in part from the project, and any news articles, brochures, seminars, or other promotional materials or media through which the grantee publicizes the Project will acknowledge the CASF's Consortia program in the following manner:

"Funding for this project has been provided in full or in part through a grant by the Rural and Urban Regional Broadband Consortia Grant Account of the California Advanced Services Fund, a program administered by the California Public Utilities Commission."



Appendix A

Application Package

[This page intentionally left blank]

CASF Consortia Grant Application Checklist

Page 1 of 1

Appendix A-1, CASE CONSORTIA GRANT APPLICATION CHECKLIST To assist the Commission in verifying the completeness of your application, mark the box to the left of each item submitted with your application. For detailed requirements, please check the referenced sections of CPUC Decision (D.) 22-05-029, Appendix 3, Rural and Urban Regional Broadband Consortia Grant Account Application Requirements and Guidelines. Tab # / Form Template Included? D.22-05-029 No form, submit the information on this Name of Applicant Sec VI.A. checklist form Address Line 1 Address Line 2 City State ZIP Code Website Address Phone Number No form, submit the information on this Sec VI.A. Key Consortium Contact Information checklist form First Name Last Name Address Line 1 Address Line 2 City ZIP Code Email Address Phone Number Sec VI.A Description of existing and past non-CASF funded projects Tab 2 Non-CASF Prjs No form, submit the information as a Sec VLA Governing Board Structure separate attachment Identification of each Consortium member, background, and role Sec VI.A. Tab 3 Board Members in the proposed project No form, submit the information as a Sec VI.C. Copy of most recent Audit Report separate attachment No form, submit the information as a Sec VI.A. Proposed Broadband Project Description separate attachment Description of geographical regions/population groups/community No form, submit the information as a interests, e.g. maps, Census Block Groups, and ZIP Codes to be Sec VI.A. separate attachment covered by the proposed project No form, submit the list as a separate attachment; applicant may choose not A list identifying endorsements received from the state or local to submit endorsement letters, and government, community groups, and anchor institutions Sec VII. instead of submitting a list identifying supporting the application which organizations provide endorsement support for the applicant. Annual Work Plan and Work Plan 10 Sec VI.B. Performance Metrics Plan No form, submit the information on this 11 Sec VI.B. Name of Proposed Project checklist form Tabs 5 Budget_Obj1 thr Budget
thr 10 Obi6

No form, submit the information on this
checklist form Sec VI.D., IX., 12 П Proposed Budget Sec VI.E. Name of Fiscal Agent Address Line 1 Address Line 2 City State ZIP Code Website Address Phone Number No form, submit the information on this Sec VI.E. Key Fiscal Agent Contact Information checklist form First Name Last Name Address Line 1 Address Line 2 City State ZIP Code Email Address Phone Number Sec VLF 15 Letter Committing to Act as Fiscal Agent separate attachment - must include: (1) the name and contact information of the responsible party within the agency, including the person responsible for the administrative tasks, if different; (2) affirmation that the work outlined in the Consortium Work Plan will be completed and verification by an Annual Audit instead of the previously required Attestation Report, to be prepared by an independent, licensed Certified Public Accountant will be submitted annually to the Communications Division; and (3) the Consortium's acceptance of the Fiscal Agent's rights, duties, and responsibilities. Sec VLF Notarized Affidavit Tab 11 Affidavit Form

Appendix A-2 Description of Existing and Past Non-CASF Funded Projects

	T NON-CASF FUNDED PROJECTS [see Sec 1.6 A & 1.6 D
	nore columns and rows as needed]
Name of Consortium:	0
Name of Non-CASF Project #1:	
- Project Description	
- Project Budget	
- Project Timeline	
- Project Funding Source	
- Explain why there will be no overlap and/or duplication of such projects (i.e., provide description of geographic region served and geographic region that will be served, etc.)	
- Project Best Practices Learned	
- Other Information	
Name of Non-CASF Project #2:	
- Project Description	
- Project Budget	
- Project Timeline	
- Project Funding Source	
 Explain why there will be no overlap and/or duplication of such projects (i.e., provide description of geographic region served and geographic region that will be served, etc.) 	
- Project Best Practices Learned	
- Other Information	
Name of Non-CASF Project #3:	
- Project Description	
- Project Budget	
- Project Timeline	
- Project Funding Source	
- Explain why there will be no overlap and/or duplication of such projects (i.e., provide description of geographic region served and geographic region that will be served, etc.)	
- Project Best Practices Learned	
- Other Information	

Appendix A-3 Board member Background and Project Role

				AND PROJECT RO	LE	
	[Con	sortium Members, in	sert more columns ar	nd rows as needed]		
Name of Consortium:	0					
Name of Project:	0					
Company/Organization						
Telecommunications carrier certificated by or registered with CPUC? (yes, no, n/a)						
- If so, identify Utility Identification number						
Website Address						
First Name						
Last Name						
Address Line 1						
Address Line 2						
City						
State						
ZIP Code						
Email Address						
Phone Number						
Background (attached separate pages, in needed)						
Role in the Proposed Project						

Appendix A-4 Work Plan and Performance Metrics Plan

	10-			RK PLAN AND PERFORMA				Ji., _1			
Name of Consortium	[C0	<mark>nsortium Members, create a separat</mark> <mark>0</mark>	e work pr	an and performance metrics p	ian for each v	work plan ye	ar, ii seeking mulu-year lun	aingj			
		0									
	iect:										
Broadband deployment ac	tivities	If checked, explain why there is no funding duplication:									
	☐ triex										
onfirmation that CASF consortium udget does not duplicate any other ources of funding Objective Activity 1 Activity 1 Activity 2 Activity 2 Activity 3 Activity 4 Activity 4 Activity 4 Activity 5 Activity 4 Activity 5 Activity 4 Activity 4 Activity 4 Activity 5 Activity 4 Activity 5 Activity 4 Activity 6 Activity 7 Activity 8 Activity 9 Activity 9 Activity 1 Activity 1 Activity 1 Activity 3 Activity 3 Activity 4 Activity 5 Activity 4 Activity 4 Activity 5 Activity 1 Activity 1 Activity 2 Activity 4 Activity 2 Activity 4 Activity 5 Activity 4 Activity 5 Activity 4 Activity 4 Activity 5 Activity 4 Activity 4 Activity 5 Activity 4 Activity 5 Activity 4 Activity 5 Activity 4 Activity 5 Activity 4 Activity 4 Activity 4 Activity 5 Activity 4 Activity 4 Activity 4 Activity 4 Activity 4 Activity 5 Activity 4 Activity 5 Activity 4 Activity 4 Activity 4 Activity 5 Activity 4 Activity 4 Activity 4 Activity 5 Activity 4 Activity 4 Activity 4 Activity 4 Activity 5 Activity 4 Activity 4 Activity 3 Activity 4 Activity 3 Activity 4 Activity 4 Activity 4 Activity 4 Activity 4 Activity 3 Activity 4 Activity 3 Activity 4 Acti				Year [see instructions below for w	1 [specify: Ca ork plan termin		ions and requirements]				
Objective		Activity Description	Start-Up Activity	Deliverable(s) *	Beginning Month	End Month	Performance Measure(s)*	Method for Performance Tracking and Measuring	Responsible Party(ies)		
	Activity 1	Example: utilize the Commission's broadband maps as relevant to the geographical areas		Example: Regional broadband deployment current state assessment analysis			Examples: 1. # of mapping data updates 2. # of community outreach	[Specify performance measure data tracking and measuring methodology]			
the Commission and other state agencies to engage regional consortia, local officials, ISPs,	Activity 2	Example: identify the Commission's mapping data improvement and work with the Commission to update the data/map		Example: broadband mapping data updates and feedback			campaigns 3. # of surveys of community- based organizations 4. # of public feedback				
stakeholders, and consumers regarding priority areas and cost- effective strategies to achieve the	Activity 3	Example: conduct marketing and outreach		Example: marketing & outreach materials and outreach summary			surveys				
broadband access goal	Activity 4	Example: collect public feedback		Example: public feedback surveys							
	Activity 5										
		E and a short and a black and a black		E			[Iro:tt			
CASF infrastructure projects or	Activity 1	Example: gather market data, undertake studies to identify priority areas		Example: report of priority areas			Examples: 1. # of priority areas identified 2. # of broadband provider	[Specify performance measure data tracking and measuring methodology]			
projects related to new programs created under SB 156 and AB	Activity 2	Example: identify broadband provider offerings and identify key anchor institutions in consortia areas		Example: broadband provider offering analysis; key anchor institution analysis			offerings identified 3. # of key anchor institutions identified				
opportunities, where ISPs can expand and improve their	Activity 3	Example: develop gap analysis or other relevant analyses		Example: gap analysis report and other relevant analysis reports			4. # of CASF infrastructure projects identified 5. # of other opportunities				
offerings to achieve the goal of	Activity 4	Example: identify CASF infrastructure projects		Example: proposals of CASF infrastructure projects			identified				
reaching 98% broadband deployment in each consortia region	Activity 5	Example: identify other opportunities (i.e., leverage funding, collaborating with other stakeholders)		Example: description of other opportunities							
				Constitution 1997			Examples:	[Cnooif unorformana			
	Activity 1	Example: develop and implement cost- effective strategies for broadband deployment		Example: broadband deployment cost-effective strategy plan and strategy implementation progress reports			# of cost-effective strategies developed and implemented # of infrastructure	[Specify performance measure data tracking and measuring methodology]			
Objective 3, Assisting potential CASF infrastructure applicants or potential applicants for broadband deployment projects related to the new programs created under SB 156 and AB 164 in the project	Activity 2	Example: provide information and data about broadband availability and demand aggregation to ISPs, and inform them about CASF and assist them in identifying CASF project areas		Example: Progress reports on cost-effective strategy implementation			applications assisted 3. # of ISPs assisted				
development or grant application process	Activity 3	Example: work with ISPs to develop projects and grant applications		Example: description of infrastructure application development							
	Activity 4										
	Activity 5		П								

Work Plan and Performance Metrics Plan(continued)

Page 2 of 2

Objective 4, Conducting activities that will lead to or that and he reasonably expected to ead to CASF infrastructure orgects or broadband deployment projects related to new programs created under SB 156 and AB 164, including the Federal Funding Account, Middle- dille, Broadband Loan Loss	Activity 1	Example: support project permitting activities	Example: description of activities performed and results achieved	Examples: 1. # of project permits supported	[Specify performance measure data tracking and measuring methodology]	
		Example: engage stakeholders to better understand and explain regional broadband needs and solutions and providing technical assistance to such entities	Example: description of activities performed and results achieved	2.# of stakeholders engaged 3.# of inventories of public assets and aggregate demand updated 4.# of broadband availability	9,1	
	Activity 3	Example: conduct an inventory of public assets and aggregate demand	Example: public assets inventory updates; regional broadband availability maps	maps developed		
	Activity 4					
	Activity 5					
	Activity 1	Example: publicize wireline testing volunteer requests	Example: publicizing materials and list of testing volunteers	Examples: 1.# of wireline testing	[Specify performance measure data tracking and	
Objective 5, Assisting the	Activity 2	Example: assist volunteers in wireline testing	Examples: Wireline testing training materials	conducted 2. # of mapping data updates	measuring methodology]	
Commission in publicizing requests for wireline testing	LACTIVITY 3	Example: collect and analyze wireline testing data	Example: Wireline testing data analysis	identified as a result of testing		
volunteers in areas, as needed	Activity 4					
	Activity 5					
Conducting and Submitting annual audit reports, as required	Annual Audit	Example: provide the required annual audit report	Annual audit report	n/a	n/a	

Instructions:

instructions.	
Work Plan Terminology	Definition / Requirements
Activity	Identifying the specific work activities which must be performed in order to produce the various project deliverables/outcomes/results and achieve the CASF Consortia Grant program objectives. The CASF Consortia Grant Account will fund consortia activities directly related to and in support of CASF infrastructure applications. Please note, a Consortia Account shall not be used for adoption activities; a Consortia Account grant shall not be used for construction of infrastructure facilities; a Consortia Account grant shall not be used for construction of infrastructure facilities; a Consortia Account grant shall not be used to fund activities that already funded by any other public or private sources.
Deliverable	Identifying the specific measurable, tangible, and verifiable work products (i.e., analysis, report, map data), outcomes, and/or results that must be produced to complete the project. Attending meetings and conducting conference calls are the work effort/processes to produce the CASF Consortia Grant program deliverables, and are not considered as deliverables.
End Month)	identifying the planned beginning and end morths for performing activities and for meeting deliverables/outcomes/results. The timeline establishes the project schedule, which is used to compare actual results to the approved Work Plan to determine if preventive or corrective action is needed to meet the program objectives. The timeline should describe each of the milestones, including deliverables and performance metrics to be accomplished.
	identifying the specific, quantitative outcome/result measures which generate reliable data on the effectiveness and efficiency of program and assess how well the consortium is achieving the CASF Consortia Grant program objectives. Attending meetings and conducting conference calls are the work effort/processes to achieve the objectives, and are not considered as performance measures.
Method for Performance Tracking and Measuring	Explaining how the performance measure outcomes/results will be tracked and measured following milestone dates and/or completion of activities/deliverables, as described in the Work Plan.

^{*} Communications Division may request progress reporting and payment requests to include documentation of performance/outcomes, consistent with the application's Work Plan and Performance Metrics Plan.
** Consortia grantees may request an initial start-up cost budget, up to 25% of the entire grant.

^{***} The CASF Rural and Urban Regional Broadband Consortia Grant Account shall be available for grants to eligible consortia to facilitate the deployment of broadband services by assisting CASF infrastructure grant applicants in the project development or grant application process or assisting broadband deployment projects related to programs created under Senate Bill (SB) 156 and Assembly Bill (AB) 164.

Appendix A-5 Proposed Detailed Budget

		Appendix	A-5, PROPO	SED DETAIL	ED BUDGET	, List/describ	e activities i	n the Work P	lan.² Insert m	ore columns	and rows as	needed			
Name of Consortium:	0														
Objective 1	strategies to	rating with the Commission and other state agencies to engage regional consortia, local officials, ISPs, stakeholders, and consumers regarding priority areas and coses to achieve the broadband access goal Year1 [specify: from MM/YYYY] Year3 [specify: from MM/YYYY] Year3 [specify: from MM/YYYY]													
Budget Line Item	Activity 1	Activity 2	Activity 3	Activity 4	Activity 5	Activity 1	Activity 2	Activity 3	Activity 4	Activity 5	Activity 1	Activity 2	Activity 3	Activity 4	Activity 5
Personnel/ Staff Compensation															
inclusive of all benefits, payroll															
taxes, contributions, etc. (Attach															
personnel names, titles, bio, and															
position descriptions															
Subtotal, Personnel Costs	\$ \$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Transportation Cost	90	ąu	40	40	ψU	φU	90	90	***	40	40	ψU	90	90	φu
Lodging															
Per Diem															
Registration Fees															
(Conferences/Conventions)															
Subtotal, Travel Expense	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Hardware	,-	,,,	1.	,,,	,,,	,,	,-	,-	,-	,,,	,,,	,-	,-	, .	
Software															
Subtotal, Equipmen	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Office Supplies/Printing/	, ,,,	70	40	***	YV	70	, ,,,	70	***	70	YV	70	70	70	Y
Postage															
Subtotal, Supplies	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Training/	90	ψU	ψU	ψU	ψU	φU	ψU	ąυ	ψU	ψU	ψU	φυ	φU	ψU	ψ
Educational Supplies															
- "															
			•												
Subtotal, Training	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Advertising Promotion															
FIUIIUIUII															
Subtotal, Promotion	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
External Consultants															
Subtotal, Consultants	\$ \$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Consortium Overhead/ Indirect	***	ψU	φU	ψU	φU	φU	\$0	\$U	ą0	ψU	φυ	φU	***	φU	ş.
Costs															
Subtotal, Overhead	1 \$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Expenses	4 30)U	ąU	ąU	ψU	JQ.	\$0	\$U	βU	\$U	şυ	\$U	ψ	ψU	30
sale Esperiore															
Subtotal, Other Expenses			\$0 C0	\$0 C0	\$0 C0	\$0		\$0	\$0 C0	\$0	\$0	\$0	\$0	\$0	\$0
Activity Total Start-up Activity	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Budget, if requesting ¹	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Daaget, II requesting															

^{1.} Consortia may request an initial start-up cost budget, up to 25% of the entire grant.
2. The CASF Rural and Urban Regional Broadband Consortia Grant Account shall be available for grants to eligible consortia to facilitate deployment of broadband services by assisting CASF infrastructure applicants in the project development or grant application process or assisting broadband deployment projects related to programs created under SB 156 and AB 164.

Proposed Detailed Budget (continued)

Page 2 of 6

		Appendix	A-5, PROPOS	SED DETAIL	ED BUDGET,	List/describ	e activities ir	the Work P	lan: Insert m	ore columns	and rows as	needed			
Name of Consortium:	0														
Objective 2			SF infrastruct and improve												ortunities,
		Year 1 [specify	: from MM/YY\	Y to MM/YYYY]	,	ear 2 [specify	: from MM/YY\	YY to MM/YYYY	/]	,	Year 3 [specify	: from MM/YY\	Y to MM/YYYY	/1
Budget Line Item	Activity 1	Activity 2	Activity 3	Activity 4	Activity 5	Activity 1	Activity 2	Activity 3	Activity 4	Activity 5	Activity 1	Activity 2	Activity 3	Activity 4	Activity 5
Personnel/ Staff Compensation inclusive of all benefits, payroll taxes, contributions, etc. (Attach personnel names, titles, bio, and position descriptions															
Subtotal, Personnel Costs	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	SI
Transportation Cost	\$U	ψU	şυ	\$U	ψU	ŷυ	\$U	ψU	şυ	\$U	ŞU	şυ	şυ	şυ	- 3
Lodging															
Per Diem															
Registration Fees, Conferences/Conventions															
Subtotal, Travel Expense	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$
Hardware Software															-
Sollware															
Subtotal, Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$
Office Supplies/Printing/															-
Postage															
Subtotal, Supplies	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1
Training/															
Educational Supplies															
	-									-					
Subtotal, Training	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	SI
Advertising	***	**	70	70	**	γυ	70	40	**	70	***	**	70	40	*
Promotion															
															<u> </u>
Subtotal, Promotion	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1
External Consultants															
Subtotal, Consultants	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1
Consortium Overhead/ Indirect															
Costs															
Subtotal, Overhead	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$
Other Expenses	şu	\$0	ąυ	şu	\$U	ψU	şu	\$U	şu	şu.	\$U	şu	şυ	φU	- Şi
															
Subtotal, Other Expenses	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Activity Total	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0	
Start-up Activity	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$I
Budget, if requesting ¹		,								,-				, ,	

Notes:
1. Consortia may request an initial start-up cost budget, up to 25% of the entire grant.
2. The CASF Rural and Urban Regional Broadband Consortia Grant Account shall be available for grants to eligible consortia to facilitate deployment of broadband services by assisting CASF infrastructure applicants in the project development or grant application process or assisting broadband deployment projects related to programs created under SB 156 and AB 164.

Proposed Detailed Budget (continued)

Page 3 of 6

		Appendix	A-5, PROPO	SED DETAILI	ED BUDGET,	List/describ	e activities in	the Work Pl	an. ² Insert m	ore columns	and rows as	needed			
Name of Consortium:	0														
Objective 3		otential CASF It or grant app	plication prod	cess		applicants fo					v programs				
			r: from MM/YYY				Year 2 [specify							Y to MM/YYYY	
Budget Line Item	Activity 1	Activity 2	Activity 3	Activity 4	Activity 5	Activity 1	Activity 2	Activity 3	Activity 4	Activity 5	Activity 1	Activity 2	Activity 3	Activity 4	Activity 5
Personnel/ Staff Compensation inclusive of all benefits, payroll taxes, contributions, etc. (Attach personnel names, titles, bio, and position descriptions															
Subtotal, Personnel Costs	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Transportation Cost Lodging Per Diem Registration Fees,	40	***	***	40	40	ψU	40	40	30	***	90	-	40	40	, , o
Conferences/Conventions															
Subtotal, Travel Expense	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Hardware Software															
Subtotal, Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Office Supplies/Printing/ Postage															
Subtotal, Supplies	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Educational Supplies															
Subtotal, Training Advertising Promotion	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
FIGHIOUGH															
Subtotal, Promotion External Consultants	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Subtotal, Consultants Consortium Overhead/ Indirect	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Costs															
Subtotal, Overhead Other Expenses	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Subtotal, Other Expenses				\$0	\$0	\$0	\$0	\$0			\$0		\$0	\$0	\$0
Activity Total Start-up Activity	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0
Budget, if requesting ¹			,		,-										

Notes:
1. Consortial may request an initial start-up cost budget, up to 25% of the entire grant.
2. The CASF Rural and Uhan Regional Broadband Consortia Grant Account shall be available for grants to eligible consortia to facilitate deployment of broadband services by assisting CASF infrastructure applicants in the project development or grant application process or assisting broadband elegion and the project development or grant application process or assisting broadband elegion and the project related under SB 156 and AB 164.

Proposed Detailed Budget (continued)

Page 4 of 6

		Appendi	ix A-5, PROP	OSED DETAIL	ED BUDGET	, List/describ	e activities in	the Work Pla	n.² Insert mor	e columns an	d rows as ne	eded				
Name of Consortium:	0															
Objective 4	Conducting and AB 164,	Conducting activities that will lead to or that can be reasonably expected to lead to CASF infrastructure projects or broadband deployment projects related to new programs created under SB 156 and AB 164, including the Federal Funding Account, Middle-Mile, Broadband Loan Loss Reserve, and Local Agency Technical Assistance														
		Year 1 [specify	/: from MM/YYY	/Y to MM/YYYY]			Year 2 [specify	r: from MM/YYY	Y to MM/YYYY]			Year 3 [specify	: from MM/YYY	Y to MM/YYYY]		
Budget Line Item	Activity 1	Activity 2	Activity 3	Activity 4	Activity 5	Activity 1	Activity 2	Activity 3	Activity 4	Activity 5	Activity 1	Activity 2	Activity 3	Activity 4	Activity 5	
Personnel/ Staff Compensation inclusive of all benefits, payroll taxes, contributions, etc. (Atlach personnel names, ttles, bio, and position descriptions																
Subtotal, Personnel Costs Transportation Cost _odging	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$	
Per Diem Registration Fees, Conferences/Conventions																
Subtotal, Travel Expense	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$	
Software																
Subtotal, Equipment Office Supplies/Printing/	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$	
Postage																
Subtotal, Supplies Training/ Educational Supplies	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$	
Subtotal, Training Advertising Promotion	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$	
Subtotal, Promotion External Consultants	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$	
Subtotal, Consultants	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$	
Subtotal, Overhead ther Expenses	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$	
Subtotal, Other Expenses Activity Total	\$0 \$0				\$0 \$0	\$0 \$0		\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0		\$0 \$0	\$0 \$0	\$	
Start-up Activity Budget, if requesting ¹	\$0				\$0	\$0		\$0	\$0	\$0	\$0		\$0	\$0	\$	

^{1.} Consortia may request an initial start-up cost budget, up to 25% of the entire grant.
2. The CASF Rural and Urban Regional Broadband Consortia Grant Account shall be available for grants to eligible consortia to facilitate deployment of broadband services by assisting CASF infrastructure applicants in the project development or grant application process or assisting broadband deployment projects related to programs created under SB 156 and AB 164.

Proposed Detailed Budget (continued)

Page 5 of 6

	Appendix A-5, PROPOSED DETAILED BUDGET, List/describe activities in the Work Plan ² Insert more columns and rows as needed														
Name of Consortium:	0														
Objective 5	Assisting th	ne Commissio	on in publiciz	ing requests	for wireline	testing volu	nteers in area	is, as needed	i						
				/Y to MM/YYYY			Year 2 [specify							YY to MM/YYYY	1
Budget Line Item	Activity 1	Activity 2	Activity 3	Activity 4	Activity 5	Activity 1	Activity 2	Activity 3	Activity 4	Activity 5	Activity 1	Activity 2	Activity 3	Activity 4	Activity 5
Personnel/ Staff Compensation															
nclusive of all benefits, payroll															
taxes, contributions, etc. (Attach															
personnel names, titles, bio, and															
position descriptions															
<u> </u>			_												
Subtotal, Personnel Costs	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$
Transportation Cost															
Lodging															
Per Diem															
Registration Fees,															
Conferences/Conventions															
Subtotal, Travel Expense	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1
Hardware															
Software															
Subtotal, Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1
Office Supplies/Printing	40	***	***	Y	ų,	40	40	¥0	70	Y	- 40	40	***	Y	Υ,
Postage															
Subtotal, Supplies	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Training/ Educational Supplies															
Luacanonar Gappines															
Subtotal, Training	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1
Advertising															
Promotion															
Subtotal, Promotion	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1
External Consultants	30	\$0	***	ψU	ψU	ąu	***	ψU	φU	ψU	ψU	30	- şu	φU	Ŷ
External Consultants															
Subtotal, Consultants	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$
Consortium Overhead/Indirect															
Costs															
Subtotal, Overhead	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$
Other Expenses	1														
Cultivial City of Free					,,,	,,,		**	,,,	**	,,				
Subtotal, Other Expenses Activity Total	\$0 \$0		\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0		\$0 \$0	\$0 \$0		\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	şı Şı
Start-up Activity														·	
Budget, if requesting ¹	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1
Dauget, II requesting															

^{1.} Consortia may request an initial start-up cost budget, up to 25% of the entire grant.

2. The CASF Rural and Urban Regional Broadband Consortia Grant Account shall be available for grants to eligible consortia to facilitate deployment of broadband services by assisting CASF infrastructure applicants in the project development or grant application process or assisting broadband deployment projects related to programs created under SB 156 and AB 164.

Proposed Detailed Budget (continued)

Page 6 of 6

Appendix A-5, PROPOSED DETAILED E	SUDGET, List/describe activit needed	ies in the Work Plan. Insert m	nore columns and rows as
	0		
Conducting and Submitting annual audit r	eports, as required ²		
	Year 1 [specify: from MM/YY to MM/YY]	MM/YY]	Year 3 [specify: from MM/YY to MM/YY]
Budget Line Item Personnel/ Staff Compensation inclusive of all benefits, payroll taxes, contributions, etc. (Attach personnel names, titles, bio, and position descriptions	Annual Audit	Annual Audit	Annual Audit
Subtotal, Personnel Costs Transportation Cost Lodging Per Diem Registration Fees, Conferences/Conventions	\$0	\$0	\$0
Subtotal, Travel Expense Hardware Software	\$0	\$0	\$0
Subtotal, Equipment Office Supplies/Printing/ Postage	\$0	\$0	\$0
Subtotal, Supplies Training/ Educational Supplies	\$0	\$0	\$0
Subtotal, Training Advertising Promotion	\$0	\$0	\$0
Subtotal, Promotion External Consultants	\$0	\$0	\$0
Subtotal, Consultants Consortium Overhead/ Indirect Costs	\$0	\$0	\$0
Subtotal, Overhead Other Expenses	\$0	\$0	\$0
Subtotal, Other Expenses Activity Total	\$0 \$0	\$0 \$0	\$0 \$0

^{1.} The CASF Rural and Urban Regional Broadband Consortia Grant Account shall be available for grants to eligible consortia to facilitate deployment of broadband services by assisting CASF infrastructure applicants in the project development or grant application process or assisting broadband deployment projects related to programs created under SB 156 and AB 164.

^{2.} Pursuant to Pub. Util. Code, § 281(g)(2), each consortium must conduct an annual audit of its expenditures and submit to the Commission an annual report that includes both of the following: (1) a description of activities completed during the prior year, how each activity promotes the deployment of broadband services, and the cost associated with each activity; and (2) the number of project applications assisted.

Appendix A-6 Affidavit Form

Page 1 of 1

Appendix A-6, AFFIDAVIT FORM

Name of Regional Consortium (Consortium):	[Title] of	
My name is[Name of local agency/town acti Consortium].	I am ng as Fiscal Agent], whi	ich is the Fiscal Agent for	[Name of
		ommission's Rules of Practice and Procedure of local agency/town acting as Fiscal Age	
Broadband Consortium Grant Ad	ecount funding under the	acts stated in this Application for the Rural as provisions of the California Advanced Serv make this Application on behalf of and to bi	rices Fund, I am
I further swear or affirm that and state statutes, rules, and regu Consortium Grant Account fund	lations covering broadb	[Name of Consortium] agrees to and services and state contractual rules and Advanced Services Fund.	comply with all federal regulations, if granted
conditions, and requirements of	he grant and thus submi	[Name of Consortium] agrees to ts to the jurisdiction of the Commission with ant Account funding from the California Ac	n regard to disbursement
or any state regulatory agency for civilly or criminally liable by a c	r failure to comply with ourt of appropriate juris or for any action which:	r, or partner oftcy; 2) was sanctioned by the Federal Commany regulatory statute, rule, or order; nor 3) diction for violation of Section 1700 et. seq. involved misrepresentation to consumers, no	has been found either of the California
		nder Rule 1.1 of the California Public Utiliti dge, all of the statements and representation	
I further swear or affirm that I ag of Practice and Procedure.	gree to comply with Rule	es 1.11 and 2.2 of the California Public Utili	ties Commission's Rules
	to Public Utilities Code	nditions of a CASF award or other program sections 2108 and 2111 for failure to meet the	
Signature and Title	_		
Type or Print Name and Title	_		
SUBSCRIBED AND SWORN	to before me on the	day of, 20	
Notary Public In and For the Sta My Commission expires:	te of:		



Appendix B

Consortia Grant Forms

[This page intentionally left blank]

Appendix B-1 Grant Disbursement Schedule Form

Page 1 of 2

California Advanced Services Fund (CASF) Rural and Urban Regional Consortia Grant Account Grant Disbursement Schedule Form

Name of Regional Consortium	
Name of Fiscal Agent (Please attach Payee Data Rec (STD 204 - Payee Data Record (ca.gov): https://www.do	
Commission Resolution awarding grant: Resolution T	Issuance Date:
Total CASF Approved Amount: \$	
Year 1 (from mm/yyyy to mm/yyyy): \$	Year 2 (from mm/yyyy to mm/yyyy):\$
Year 3 (from mm/yyyy to mm/yyyy): \$	Year 4 (from mm/yyyy to mm/yyyy):\$
Start Date of Grant (dd/mm/yyyy): Due-dates for Bi-annual Progress Reports and paymonts.	
Year 1 Report 1:	
Year 2 Report 1:	
Year 3 Report 1:	Year 3 Report 2:
Year 4 Report 1:	Year 4 Report 2:
Is a bank account solely for CASF deposits and expe	enditures established: Yes: No
If no, please explain:	
Please explain how billing to discrete funding sources	s will not overlap:
_	
Recipient Signature	Fiscal Agent Signature

Appendix B-1 Grant Disbursement Schedule Form (continued)

Page 2 of 2

Printed Name	Printed Name
Date	Date
Telephone Number (include area code): _()	Telephone Number (include area code):()
Email Address:	Email Address:

Consent Form

Name of Grantee:
The Grantee identified above hereby acknowledges receipt of the California Public Utilities Commission Resolution T and agrees to comply with all grant terms, conditions, and requirements set forth in the Resolution, as well as all CASF rules, including those in the Rural and Urban Regional Broadband Consortia Account Requirements, Guidelines and Application Materials. If applicable, Grantee must fulfill the monthly reporting requirements set forth in Public Utilities Code section 281(I)(1) if it is using a licensed contractor or subcontractor to undertake a contract or subcontract in excess of twenty-five thousand dollars (\$25,000) to perform work on a project funded or financed by CASF.
Undersigned representative of [Name of Grantee]
is duly authorized to execute this Consent Form on behalf of the Grantee and to bind the
Grantee to the terms, conditions, and requirements set forth in California Public Utilities
Commission Resolution T
Dated this day of, 20
Signature Printed Name
Title:
Organization or Name of Company
Business Address (include street address, suite/apt. number, city, state, and ZIP Code):
Telephone Number (include area code):
Email Address:

[This page intentionally left blank]



Appendix C

Bi-annual Progress Report and Payment Request Package

[This page intentionally left blank]

Appendix C-1, California Advanced Services Fund Consortia Grant Program

Bi-annual Report and Payment Request Transmittal Letter and Affidavit

Transmittal Lette	r and Affidavit
CASF Consortia Grant Administrator	
Attached are the Bi-annual Report and/or	Payment Request for:
Work Plan Year:*[e.g., Year 1, Report 1]	Reporting Period:* [specify: from mm/yy to mm/yy]
I declare under penalty of perjury under the to the best of my knowledge, all of the starthis Bi-annual Report and Bi-Annual Paym	tements and representations made in
Regional Consortium Fiscal Agent	
Signature and Title	
Print Name and Title	
Date:	
	CASF Consortia Grant Administrator Attached are the Bi-annual Report and/or Work Plan Year:* [e.g., Year 1, Report 1] I declare under penalty of perjury under the to the best of my knowledge, all of the stath this Bi-annual Report and Bi-Annual Paym Regional Consortium Fiscal Agent Signature and Title Print Name and Title

^{*} The Work Plan Year and Reporting Period should be consistent with the work plan year information listed on the *Grant Fund Request Form* (Appendix B-1).

Appendix C-2 Bi-Annual Payment Request Cover Sheet

Page 1 of 1

Appendix C-2, BI-ANNUAL PAYMENT REQUEST COVER SHEET^{1, 2}

Name of Consortium	
Approved Grant, Year 1 [specify: from MM/YY to MM/YY]	
Approved Grant, Year 2 [specify: from MM/YY to MM/YY]	
Approved Grant, Year 3 [specify: from MM/YY to MM/YY]	
Approved Grant, Year 4 [specify: from MM/YY to MM/YY]	

Reporting Period [specify: from MM/YY to MM/YY]			
Reporting Period Ending: [MMYY]			
	Amount Requested	Amount Approved	Amount Received
Start-Up Costs			
Y1 Report 1, Progress Payment			
Y1 Report 2, Progress Payment			
Y2 Report 1, Progress Payment			
Y2 Report 2, Progress Payment			
Y3 Report 1, Progress Payment			
Y3 Report 2, Progress Payment			
Y4 Report 1, Progress Payment			
Y4 Report 2, Progress Payment			
Total			

Notes:

^{1.} Consortia should submit this *Bi-annual Payment Request Cover Sheet* in Excel format.

² The Work Plan Year and Reporting Period should be consistent with the work plan year information listed on the *Grant Fund Request Form* (Appendix B-1).

Appendix C-3 Bi-annual Progress Report

			Appendix C-3, BI-A	NNUAL PROGRESS	PLAN ^{1,2}		
Name of Consortium:							
Name of Project:							
Actual Project Start Date (dd/mm/yyyy):							
Reporting Period [specify: from mm/yy to mm/yy]							
Date Report Submitted (dd/mm/yyyy):							
Goals/Objectives (as stated in the Work Plan)	Activitie	s Performed	Deliverables Completed	Completion Date (as state in approved Work Plan)	Actual Date Completed	Actual Performance Measure Results	Comments (i.e., reasons why actual activities, deliverables, completion dates, and/or performance measures not meeting approved Work Plan'
Objective 1, Collaborating with the Commission	Activity 1						
and other state agencies to engage regional	Activity 2						
consortia, local officials, ISPs, stakeholders, and consumers regarding priority areas and cost-	Activity 3						
effective strategies to achieve the broadband	Activity 4						
access goal	Activity 5						
Total, Objective 1							
Objective 2, Identifying potential CASF	Activity 1						
infrastructure projects or potential broadband deployment projects related to new programs	Activity 2						
created under SB 156 and AB 164, along with other opportunities, where ISPs can expand and	Activity 3						
improve their infrastructure and service offerings to achieve the goal of reaching 98% broadband	Activity 4						
deployment in each consortia region	Activity 5						
Total, Objective 2							
Objective 2 Assisting a security OARE	Activity 1						
Objective 3 , Assisting potential CASF infrastructure applicants or potential applicants for	Activity 2						
broadband deployment projects related to the new programs created under SB 156 and AB 164 in	Activity 3						
the project development or grant application	Activity 4						
process	Activity 5						
Total, Objective 3	-						
Objective 4, Assisting the Commission in promoting broadband deployment in California	Activity 1						
promoung broadband deployment in California and conducting activities that will lead to or that can be reasonably expected to lead to CASF	Activity 2						
infrastructure projects or broadband deployment projects related to new programs created under	Activity 3						
SB 156 and AB 164, including the Federal Funding Account, Middle-Mile, Broadband Loan Loss Reserve, and Local Agency Technical	Activity 4						
Assistance leading to CASE infrastructure applications	Activity 5						
Total, Objective 4							
	Activity 1						
Obligation Englishments Commission in	Activity 2						
Objective 5, Assisting the Commission in publicizing requests for wireline testing volunteers in areas, as needed	Activity 3						
	Activity 4						
	Activity 5						
Total, Objective 5	,						
Objective 6, Conducting and Submitting annual audit reports, as required	Annual Audit						
Total, Objective 6							
•							

Notes:

1. A Start-up Period Progress Report is required if the grantee is approved for initial start-up cost budget and requests an initial start-up cost payment, up to 25% of entire grant budget.

Consortia should sport to the completion of start-up activities per the approve Work Plan and Performance Metrics Plan, as well as milestone met

2. The CASF Rural and Urban Regional Broadband Consortia Grant Account shall be available for grants to eligible consortia to facilitate deployment of broadband services by assisting CASF infrastructure applicants in the project development or grant application process or assisting broadband deployment projects related to programs created under SB 156 and AB 164.

Appendix C-4 Bi-annual Payment Request Worksheet

	Appendix C-4, Bi-annual Payment Request ^{1, 2} (name) Broadband Consortium Work Plan Year: Reporting Period: from mm/yy to mm/yy										
Line Item #	Description	Invoice or Receipt#	Invoice or Receipt Date	Supporting Document Attached	Objective 1:	Objective 2:	Objective 3:	Objective 4:	Objective 5:	Objective 6:	TOTAL Amount
Personr	nel Costs										
1		###	(mm/dd/yyyy)		\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
2					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
3					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
4					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
5					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
	subtotal				\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
Travel E	xpense							·			
6		###	(mm/dd/yyyy)		\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
7					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
8					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
9					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
10	14-4-1				\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
	subtotal				\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
Carriana											
Equipme 11	ent	###	(mm/ddhaaa)		\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
12		11111	(mm/dd/yyyy)		\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
13					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
14					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
15					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
.,	subtotal				\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		\$0.00

Appendix C-4 Bi-annual Payment Request Worksheet (continued)

Page 2 of 3

Appendix C-4, Bi-annual Payment Request ^{1, 2}
(name) Broadband Consortium

Year: Reporting Period: from mm/yy to mm/yy Work Plan Year:

			TTOTAL IGHT		portang r or		,,	,,			
Line Item #	Description	Invoice or Receipt#	Invoice or Receipt Date	Supporting Document Attached	Objective 1:	Objective 2:	Objective 3:	Objective 4:	Objective 5:	Objective 6:	TOTAL AMOUNT
Supplies	8										
16		####	(mm/dd/yyyy)		\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
17					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
18					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
19					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
20					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
	subtotal				\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
_	Expense									44.44	
21		####	(mm/dd/yyyy)		\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
22					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
23					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
24					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
25					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
	subtotal				\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
Advantia	ing/Dromotion										
26	sing/Promotion	####	(mana (dd fi a n a r)		\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
27		******	(mm/dd/yyyy)		\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
28					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
29					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
30					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
- 30	subtotal				\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
	Subtotal				Ψ0.00	40.00	Ψ0.00	Ψ0.00	Ψ0.00	\$0.00	\$0.00
Externa	Consultants										
31		####	(mm/dd/yyyy)		\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
32					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
33					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
34					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
35					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
	subtotal				\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00

Bi-annual Payment Request Worksheet (continued)

Page 3 of 3

Appendix C-4, Bi-annual Payment Request ^{1, 2}				
(name) Broadband Consortium				
Work Plan Year:	Reporting Period: from mm/yy to mm/yy			

Line Item #	Description	Invoice or Receipt#	Invoice or Receipt Date	Supporting Document Attached	Objective 1:	Objective 2:	Objective 3:	Objective 4:	Objective 5:	Objective 6:	TOTAL AMOUNT
Overhead											
36		###	/mm/ddhaaa/\		\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
37		mm	(mm/dd/yyyy)	-	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
38					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
39					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
40					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
40	subtotal				\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
	Subtotal				40.00	Ψ0.00	\$0.00	40.00	ψ0.00	Ψ0.00	Ψ0.00
Meetings/	Conferences/Conventions										
41		####	(mm/dd/yyyy)		\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
42					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
43					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
44					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
45					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
	subtotal				\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
Other Exp	penses										
46		####	(mm/dd/yyyy)		\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
47					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
48					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
49					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
50					\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
	subtotal				\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
	GRAND TOTALS				\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00

Notes:

^{1.} Consortia should submit this bi-annual payment request in Excel format.

^{2.} Consortia should clearly identify requested start-up activity costs on this payment request, if Consortia is approved for initial start-up cost budget.

Appendix C-5 Public Workshop Reimbursement Request Form

Appendix C-5, PUBLIC WORKSHOP REIMBURSEMENT REQUEST FORM			
Name of Consortium			
Date of Public Workshop			
Location of Public Workshop (City)			
	•		

Name of Delegate	Requested Amount Please attach a Travel Request Form, STD 262-A (https://www.documents.dgs.ca.gov/dgs/fmc/pdf/std262a.pdf) for each claimant			
Total				



Appendix D

Annual Audit Report Template for Reporting Activity Information

[This page intentionally left blank]

Appendix D Annual Audit Report Template for Reporting Activity Information

Page 1 of 1

Annual Audit Report Template for Reporting Activity Information as Required by Assembly Bill (AB) 1665

[Consortium Name]
Notes for Financial Statements
For the Project Year Ended [Month Date, Year]

Note # - Specific Activities

Specific activities for [Consortium Name] for the project year ended [Month Date, Year] are as follows:

Objective Description	Description of Activities Completed During the Prior Year	How Each Activity Promotes the Deployment of Broadband Services	Cost Associated with Each Activity
	Activity 1		
Objective 1, Collaborating with the Commission and other state agencies to engage	Activity 2		
regional consortia, local officials, ISPs, stakeholders, and consumers regarding	Activity 3		
priority areas and cost-effective strategies to achieve the broadband access goal	Activity 4		
	Activity 5		
Objective 2, Identifying potential CASF infrastructure projects or potential	Activity 1		
broadband deployment projects related to new programs created under SB 156	Activity 2		
and AB 164, along with other opportunities, where ISPs can expand and improve	Activity 3		
their infrastructure and service offerings to achieve the goal of reaching 98%	Activity 4		
broadband deployment in each consortia region	Activity 5		
Objective 3, Assisting potential CASF infrastructure applicants or potential	Activity 1		
applicants for broadband deployment projects related to the new programs	Activity 2		
created under SB 156 and AB 164 in the project development or grant application	Activity 3		
	Activity 4		
process	Activity 5		
Objective 4, Conducting activities that will lead to or that can be reasonably	Activity 1		
expected to lead to CASF infrastructure projects or broadband deployment	Activity 2		
projects related to new programs created under SB 156 and AB 164, including the	Activity 3		
Federal Funding Account, Middle-Mile, Broadband Loan Loss Reserve, and Local	Activity 4		
Agency Technical Assistance	Activity 5		
	Activity 1		
Objective 5, Assisting the Commission in publicizing requests for wireline testing	Activity 2		
volunteers in areas, as needed	Activity 3		
	Activity 4		
	Activity 5		
Objective 6, Assisting the Commission in promoting broadband deployment in	Activity 1		
California, related to the Federal Funding Account and other programs including	Activity 2		
Middle-Mile, Broadband Loan Loss Reserve, and Local Agency Technical Assistance	Activity 3		
created under SB 156 and AB 164.	Activity 4		
	Activity 5		

Note # - The number of project applications assisted.

Project Application Assisted	Priority Area(s)
[Project application name]	[List priority areas]
[Project application name]	[List priority areas]
[Project application name]	[List priority areas]
[Project application name]	[List priority areas]
[Project application name]	[List priority areas]

otal number of project applications assisted	
